

-41-

Title of the project:- C/O Link Road From Kanda To Seri Dagain KM 0/0 to 3/700.

MUCK MANAGEMENT PLAN (MNP)

Sr.	Description	Quantity
1	Total Quantity of Muck being produced	20000.00
2	Deduction for useful stone as required under thw clause of agreement to be exctued by the Contractor and Executieve Engineer of Project. 3% 14000.00cum	6000.00
3	Net Balance Quantity of Debriess/Muck (1-2)	14000.00
4	Quantity available on site with swell factor @ 60% 1.60A (B)	19999.4
	Total (sr.3+4)	33999.4cum(B)
5	Material /Muck to be used in Project:-	
(i)	Deduction of material required for the construction of dumping place in dry masonry wall/Edge wall @ 40% of (B)	13599.76
(ii)	Less for material/Muck required for leveling of the proposed road for the construction @12% of (B)	4079.92
(iii)	Less for material /Muck required for the construction of the proposed road on the analogy of half cutting half filling @ 30% of (B)	10199.82
	Total :- (i)+(ii)+(iii)	27879.5 Cum (C)
6	Net material/Muck to dumped in dumping site (B-C) in Cum	6101.9 cum

Proposed dumping sites

Material/Muck left at the site which required carriage for the proper dumping at the recognized site as per the instructions of forest and environment Ministry reinforced by various judgments of the Apex Court Govt. of india.

Sr. No.	Dumping Site No.	Kh no.	Design Annexed Yes/No.	Capacity
1.	1	71/1	yes	6,240.00 CUM
			Total	6,240.00 CUM



Gs
Divisional Forest Officer
Shimla Forest Division

Assistant Engineer
Junga (B & R) Sub- Division
H.P.P.W.D., Junga

Executive Engineer
Shimla Division No.-1
H.P.P.W.D., Shimla-3

Muck Dumping Plan Clo Proposed link Road Jeomun Sezi Degain 0/0 to 3/700kmm

Not to Scale
↑

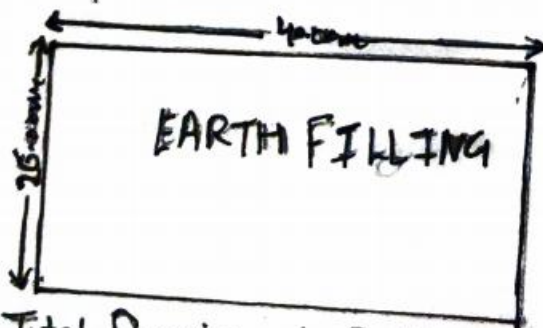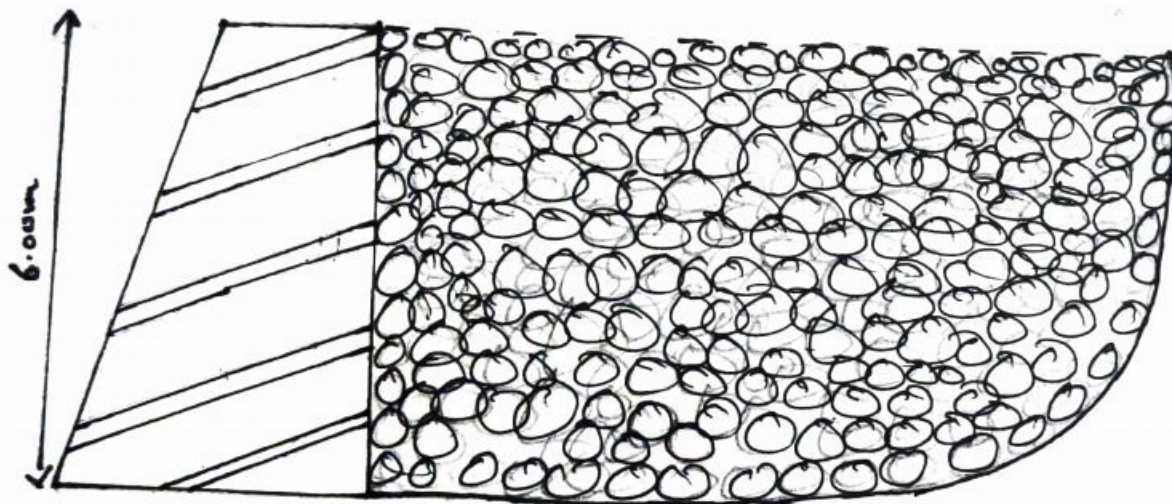

Total Dumping	L	B	H
Dumping site	40	26	6
Capacity	6,240 CUM		

[Signature]
Assistant Engineer
Junga (B & R) Sub-Division
H.P.P.W.D., Junga

[Signature]
Executive Engineer
Shimla Division No.-1
H.P.P.W.D., Shimla-3
