

2119


मलुवा निस्तारण प्रमाण-पत्र

परियोजना का नाम :- माननीय मुख्यमंत्री घोषणा संख्या 229/2015 के अन्तर्गत जनपद अल्मोड़ा में विधानसभा क्षेत्र रानीखेत में गनियाद्योली-विशालकोट मोटर मार्ग का ग्राम टाना तरस्वार कोठिया डौनी होते हुए विशालकोट की ओर 3 किमी. मोटर मार्ग (3.00किमी.)(0.900है0)

प्रमाणित किया जाता है कि उक्त मार्ग के नव निर्माण के दौरान उत्पादित मलवे के निस्तारण हेतु मलवा निस्तारण योजना संलग्न है।


J.E


सहायक अभियन्ता,
प्रान्तीय खण्ड, लोक निर्माण विभाग,
रानीखेत


अधिशारी अभियन्ता,
प्रान्तीय खण्ड, लोक निर्माण विभाग,
रानीखेत

[INDEX]

Name of Work : Extension of Ganidhyoli Vishalkote motor road via Tana, Taraswar, Kothiya, Doni to Vishalkote.

SL NO.	DESCRIPTION	PAGE NO.	
		FROM	TO
1	TITLE PAGE		
2	DISPOSAL PLAN		
3	OWNER'S DETAIL		
4	ANALYSIS OF RATES		
5	DETAIL OF MEASUREMENT		
6	BILL OF QUANTITY		

सहकार अफिसर
ग्रामीण खण्ड, लो. नि. वि. ०
रानीखेत

MUCK DISPOSAL PLAN

Name of Work : Extension of Ganidhyoli Vishalkote motor road via Tana, Taraswar, Kothiya, Doni to Vishalkote.

Total Length of Motor Road : 3.000Km

Length passing through Nap Land : 2.000 Km

Length passing through Forest Land : 1.000 Km

Sl.No.	Material Received from hill side cutting	Qty	Unit
1	b		Cum
2	Km 1 to 3 1/2(1000X6X3)	9000.00	Cum
		9000.00	Cum
	40% for swell factor	3600	Cum
	Total	12600.00	Cum

Disposal and Use of Material

1	Retaining Wall 1600X(0.60+1.6)/2X3	5280.00	Cum
2	Breast Wall 1250(0.60+0.90)/2X1.80	1687.50	Cum
3	H.P. Stone Filling 3X8X13.125	315.00	Cum
4	Costruction of Scupper 3X8X37.09	890.16	Cum
5	Soling Work 1100X4.05X0.12	486.00	Cum
6	Costruction of Pucka Drain	0.00	Cum
7	Total Used	8658.66	Cum
8	Material Disposed by Cartage in Dumping Yard	3941.34	Cum

Location and Quantity of Dabries Disposal

Locati on of dumpi ng	Size of Dumping Yard	Type of Land	Capacity of dumping yard(cum)
Km 1	120.00X10.00X3.50	Nap Land	4200.00
	Total		4200.00

Summary of Dabries Disposal

S.No.	Total Dabries	Material disposal by Cartage	Reused material for road construction	Disposed & Dumping Zone	Balance dabries
1	12600.00	3941.34	8658.66	3941.34	Nil

सहायक अभियन्ता,
प्रान्तीय खण्ड, लो०नि०वि०,
रानीखेत।

अधिशारी अभियन्ता,
प्रान्तीय खण्ड, लो०नि०वि०,
रानीखेत।

Details of Muck Disposal Yards with land owner detail

Name of Work : Extension of Ganidhyoli Vishalkote motor road via Tana, Taraswar, Kothiya, Doni to Vishalkote.

Sl.No.	Chainage	Name of land owner & villege	Land (in Hec.)	Land (in sqm)	Land area being used for dumping yard	Longitude	Latitude
1	KM 2	Girish-Singh S/O Shri Diwan Singh	0.1820	1820.00	1200.0000	29°35'41.38"N	79°26'16.22" E
				Total	1200.0000		
				Say	0.1200		


 सहायक अभियन्ता,
 प्रान्तीय खण्ड, लो०नि०वि०,
 रानीखेत।


 अधिशासी अभियन्ता,
 प्रान्तीय खण्ड, लो०नि०वि०,
 रानीखेत।


 Girish Singh S/O
 Shri Diwan Singh


 Arvind/Ameen work/D:Excelwork


 Virendra


 Ramesh

Analysis of rate

Name of Work : Extension of Ganidhyoli Vishalkote motor road via Tana, Taraswar, Kothiya, Doni to Vishalkote.

- 1- Excavation in foundation for retaining walls in all type of soils and rocks including lead, lift and disposal surplus material as per direction of engineer in charge.

Rate as per Roads & Bridges SOR Si No. 75476 16-1 =Rs **256.90 Per Sqm**

- 2- Random Rubble Masonary laid dry in breast wall, retaining wall, parapets, scupper etc. Including supply of all materials, labour, T&P & royalty etc, required for proper complition of work. (As per PWD Uttarakhand specifications).

Rate as per Roads & Bridges SOR Si No. 75478 16-3 =Rs **1844.20 Per Sqm**


JE


खण्डक अधिकारी
प्रान्तीय खण्ड, लो० वि० वि०
रानीखेत


अधिशाली अभियन्ता
प्रान्तीय खण्ड, लो० वि० वि०
रानीखेत

Details of Measurement

Name of Work : Extension of Ganidhyoli Vishalkote motor road via Tana, Taraswar, Kothiya, Dõni to Vishalkote.

S.No.	Item of Work	Detail of Measurement					unit
		No.	Length	Width	Height	Qty	
1	Excavation in foundation for retaining walls in all type of soils and rocks including lead, lift and disposal surplus material as per direction of engineer in charge. (for 90X15X2.5)						
	Dumping Yard 1 (Km 1.00)						
	Long wall	1X1	120.00	1.93	0.50	115.80	
	Short wall	1X2	9.40	1.93	0.50	18.14	
				Total		133.94	cum
2	Random Rubble Masonary laid dry in breast wall, retaining wall, parapets, scupper etc. Including supply of all materials, labour, t&p & royalty etc, required for proper completion of work. (As per PWD Uttarakhand specifications)						
	Dumping Yard 1 (Km 1.00)						
	Long wall	1X1	120.00	(0.6+1.93)/2	4.00	607.20	cum
	Short wall	1X2	9.40	(0.6+1.93)/2	4.00	95.13	cum
				Total		702.33	cum


 सहायक अभियन्ता
 प्रान्तीय खण्ड, लो0नि0वि0,
 रानीखेत


 अधिशासी अभियन्ता
 प्रान्तीय खण्ड, लो0नि0वि0,
 रानीखेत

BILL OF QUANTITIES

Name of Work : Extension of Ganidhyoli Vishalkote motor road via Tana, Taraswar, Kothiya, Doni to Vishalkote.

Sl. No.	Name of Item	Qty.	Unit	Rate	Per	Amount
1	2	3	4	5	6	7
1	Excavation in foundation for retaining walls in all type of soils and rocks including lead, lift and disposal surplus material as per direction of engineer in charge.	133.94	cum	256.90	cum	34409.70
2	Random Rubble Masonary laid dry in breast wall, retaining wall, parapets, scupper etc. Including supply of all materials, labour, t&p & royalty etc, required for proper completion of work. (As per PWD Uttarakhand specifications.	702.33	Cum	1844.20	Cum	1295233.30
					Total	1329643.00


JE

सहायक अभियन्ता
प्रान्तीय खण्ड, लो०नि०वि०,
रानीखेत


तहसीलदार
रानीखेत (उत्तराखण्ड)


अधिशासी अभियन्ता
प्रान्तीय खण्ड, लो०नि०वि०,
रानीखेत


अधीनस्थ अभियन्ता


अधीनस्थ अभियन्ता
अलमोड़ा दक्षिण-प्रभाग


अधीनस्थ अभियन्ता
अलमोड़ा दक्षिण-प्रभाग


अधीनस्थ अभियन्ता


अधीनस्थ अभियन्ता
रानीखेत


अधीनस्थ अभियन्ता
अलमोड़ा

सहमति प्रमाण पत्र

परियोजना का नाम :- गानिधादौली-विशालकोट मोटर मार्ग का
ग्राम टना तरस्वार कीदिया डीनी होते हुए
विशालकोट की ओर 3 किमी मोटर मार्ग
जनपद अल्मोड़ा में उपरोक्त परियोजना

..... मोटर मार्ग का नव निर्माण
हेतु जो भूमि निर्माण/मलुवा निस्तारण (Muck Disposal) हेतु प्रस्तावित की गयी है उस
परियोजन हेतु यदि मेरी भूमे अर्जित की जाती है तो मुझे कोई आपत्ति नहीं है। मैं
विभागीय दरों पर अपनी भूमि सहर्ष देने को सहमत हूँ।

भवदीय,


नाम

ग्राम

क्रास सैक्शन किमी 2.00 पर प्रस्तावित मलुवा निस्तारण
(Muck Disposal) हेतु कास्तकार श्री गिरीश सिंह पुत्र श्री दिवान सिंह
..... ग्राम तरस्वार पटवारी क्षेत्र पन्थाली तहसील रानीखेत
..... के नाम भूमि विवरण निम्नप्रकार है।

क्र.सं०	खाता/खसरा नम्बर	भूमि (है०)
1.	3/3681	0.038
2.	3728	0.053
3.	3731	0.091
4.		/
5.		0.0182

मार्ग का कार्य का नाम :- हाना लम्बाट कालिया हानी हान हल विशालकाज की आर माटर निर्माण

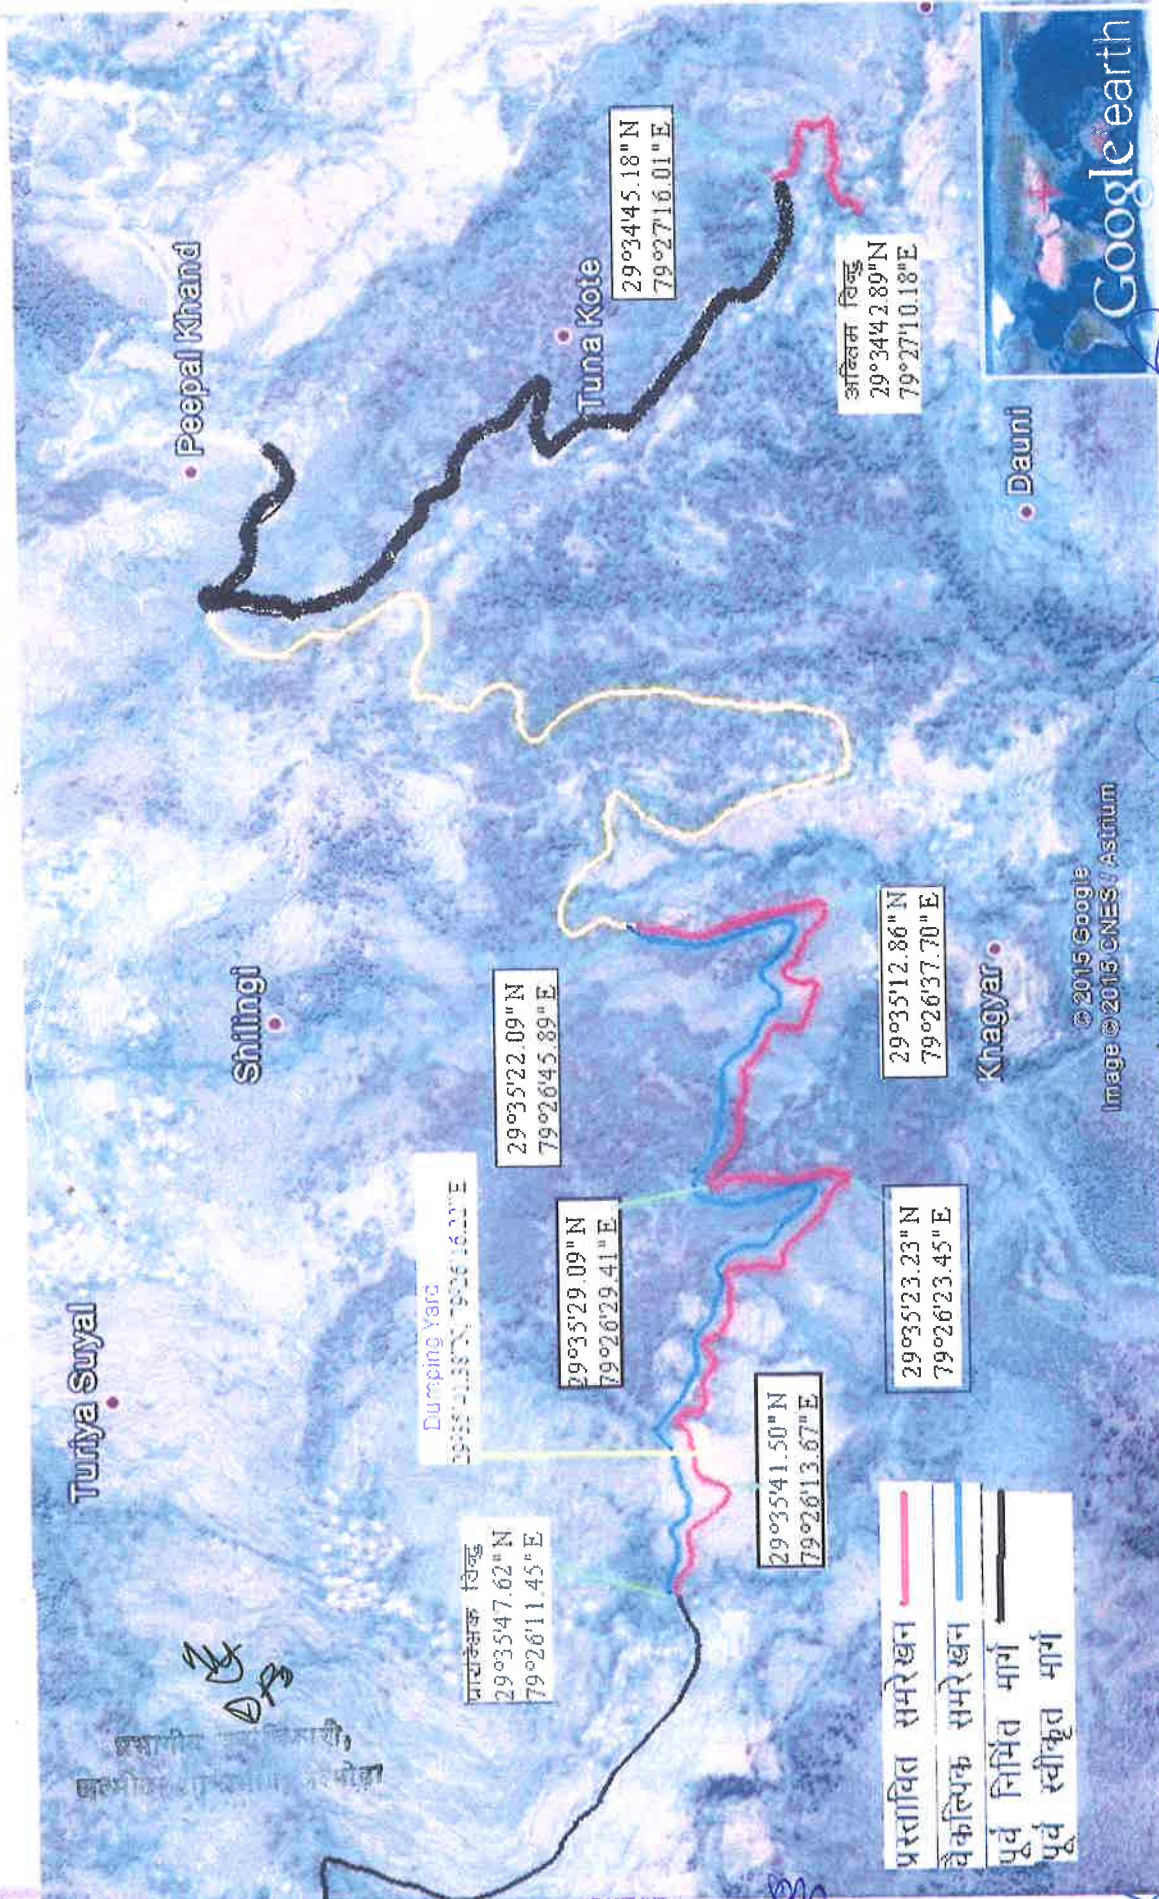

अधिसूचना, अतिरिक्त, अतिरिक्त

खिला अधिकार
बलमोडा
