

NAME OF WORK :- जनपद-चमोली के अन्तर्गत वि.सू. नं. बगड के चारमगाड -
कोटमिला (रेड) मोटर मार्ग निर्माण हेतु
प्रस्तावित डम्पिंग थार्ड (बक डिस्पोजल) स्थल
का फोटोग्राफ

46



Shy-
APR

Shy-
APR





Shy-
APR

Shy-
APR

47

NAME OF WORK :- MUCK DISPOSAL PLAN AND CROSS SECTION

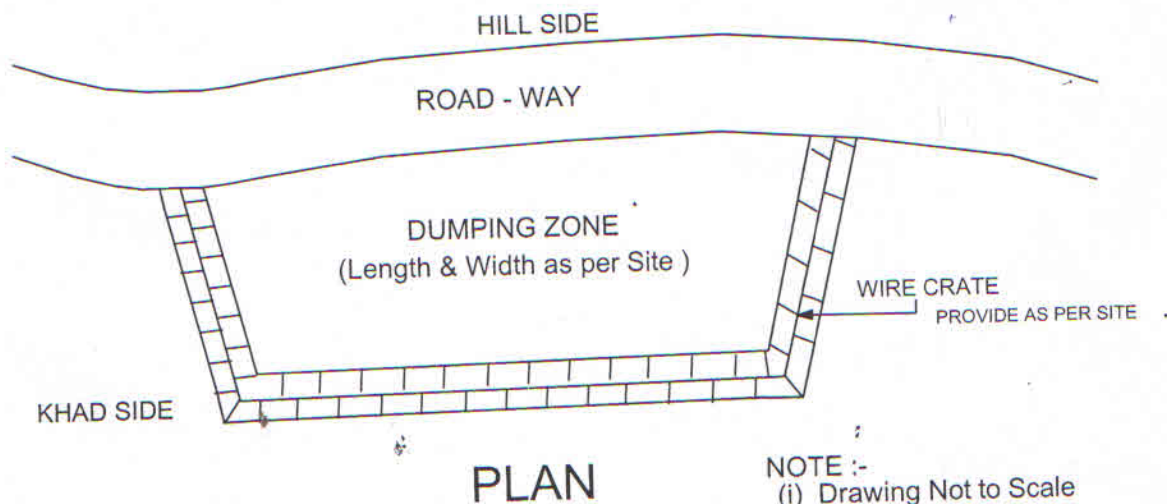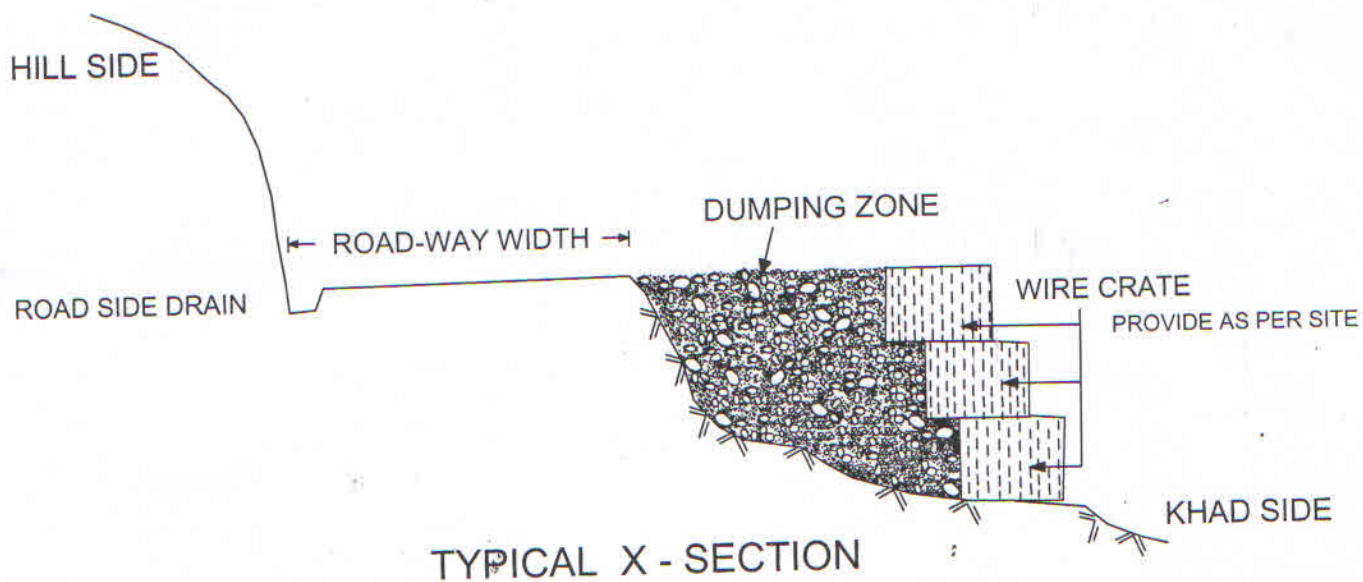

NOTE :-
(i) Drawing Not to Scale
(ii) All Dimension are in meter

Signature
J.P.E.
RWD

Signature
A.R.

DETAIL OF MUCK DISPOSAL SITE

Location of the dumping yard	Owner Of The Land	Khasra No.	Area Of The Land			Height Of the Dumping Zone (M)	Volume Of Dumping Zone	Longitude/ Latitude
			Length (M)	Width(M)	Area (In hectares)			
0/0	Gairvaram Vaan Panchayat	250,125,022,503	70.5	20	0.141	3.00	4230.00	79 25 39.46" E, 30 4 44.49"N
0/33 , 0/34	Raj Civil	2 ½	92	15	0.138	2.70	3726.00	79 25 29.08" E, 30 4 33.40"N
TOTAL			0.279			7956.00		
			Hectares			Cum		


 A. Asstt. Engr.
 R.W.D.


 Asstt. Engr.
 R.W.D.
 Sub Div. Tharali


 Ex. Engineer
 R.W.D.
 Div. Chamoli

48

Name Of Work :- construction Of Village Road at Vaaram gaad to Kotmila (Rai)
of Narayan Bagar Block

Dumping Yard

Material Recieved Due to Hill Side Cutting :- 10920.00 Cum
Add Swell Factor @ 40% :- 4368.00 Cum
Total :- 15288.00 Cum

Use Of Material

Si.No.	Item For which material is to be used	Quantity Of Material Consumed (In Cum)
1	Stone Masonry / B.Wall	1240.10 Cum
2	Hand Packed Stone Filling	1660.70 Cum
3	Construction Of Wire Crates	659.00 Cum
4	Solling	1480.20 Cum
5	Construction Of Parapets	410.00 Cum
6	Construction Of Road Side Drain	390.00 Cum
7	Construction Of Scuppers	486.00 Cum
8	Concreat Work	66.00 Cum
9	Patri Filling	940.00 Cum
	Total	7332.00 Cum

Total Material Consumed in Cum

Balance Material Left for Disposal = 15288.00 - 7332.00 = 7956.00

As per the attached Detail , the capacity of the dumping Zone = 7956.00 Cum


A. Asstt. Er./J. Er.
R.W.D.


Asstt. Er.
R.W.D.
Sub Div. Tharali


Ex. Engineer
R.W.D.
Div. Chamoli
