


MUCK DISPOSAL EXERCISE INDEX

NAME OF WORK :- CONSTRUCTION OF HUDOLI TO BINGADERA
MALLA MOTOR ROAD FOR STAGE-I WORK
UNDER C.D. PWD PUROLA (UTTARKASHI)


1. C.D. PWD PUROLA, MUCK DISPOSAL ANNEXURE-I
2. DETAILS OF MUCK DISPOSAL YARDS WITH LAND OWNERS
ANNEXURE-II



Junior Engineer
Const. Div. PWD Purola




Assistant Engineer
Const. Div. PWD Purola



Executive Engineer
Const. Div. PWD Purola



उप प्रभागीय वनधिकारी
टोन्स वन प्रभाग
पुरोला (उत्तराखण्ड)



प्रभागीय वनधिकारी
टोन्स वन प्रभाग
पुरोला (उत्तराखण्ड)


MUCK DISPOSAL/MANAGEMENT PLAN FOR HUDOLI TO BINGADERA MALLA MOTOR ROAD FOR STAGE-I WORK UNDER C.D. PWD PUROLA (UTTARKASHI)


MUCK DISPOSAL PLAN PREPARED AS FOLLOWING :-


- 1- CALCULATION OF MUCK TO GENERATE INCLUDING SWELL FACTOR
TOTAL MUCK GENERATED DURING CONSTRUCTION OF ROAD=19256.63 CUM
- 2- QUANTITY OF MUCK TO BE UTILIZED IN THE PROJECT ACTIVITIES
AS PER ATTACHED SHEET= 9251.25 CUM
- 3- BALANCE QUANTITY OF MUCK WHICH REQUIRED FOR DISPOSAL/
MANAGEMENT PLAN
(19256.63-9251.25 CUM)= 10005.38 CUM
- 4- CARRIAGE OF MUCK FROM THE MUCK GENERATION SITE TO DUMPING
SITE
MUCK WILL BE CARRY BY CONTRACTOR AS THEIR OWN COST AS PER BOND
CONDITION
- 5- OWNERSHIP OF LAND AND THE CONSENT OF LAND OWNER
MUCK WILL BE DUMP ON RESERVE FOREST/CIVIL SOYAM LAND AS
ATTACHMENT OF RECORD, PHOTO GRAPHS ALWAYS ATTACHEND AS PER
CARRYING CAPACITY. CAPACITY OF DUMPING ZONE TO BE PREPARED ON
RESERVE FOREST/CIVIL SOYAM LAND IS "10025.00 CUM" BUT REQUIRED
QYANTITY IS ONLY "10005.38 CUM " CONSENT OF LAND OWNER
ATTACHED WITH PROPOSAL.
- 6- DEVELOPMENT OF DUMPING SITE CONSTRUCTION OF RETAINING WALLS AND
OTHER STRCCTURE.
COST OF PROTECTION WORK I.E. R/WALL WIRE CRATES ETC. AGAINST
MUCK DUMPING POINT IN NAAP LAND WILL BE CONSTRUCT BY USER
AGENCY C.D. PWD PUROLA AS PROPOSED MUCK DUMPING POINT
- 7- REHABILITATION OF DUMPING SITE LIKE LEVELING
REHABILITATION OF DUMPING SITE LIKE LEVELING BY CONSTRUCTION
AGENCY C.D. PWD PUROLA
COST OF DUMPING SITE :- WE PROPOSED THE DUMPING SITE ON NAAP
LAND AREA, SO PROTECTION WORO WILL BE CONSTRUCT AS PER THEIR
SITE REQUIRMENT


UNDERTAKEN AS PER FOLLOWING BY USER AGENCY (C.D. PWD PUROLA)


- 1- MUCK MANAGEMENT PLAN WILL BE INPLEMENTED BY C.D PWD
PUROLA. IN CASE NON INPLEMENTATION OF PLAN WE WILL BE LIABLE
TO PENCLTY/ACTION
- 2- THE PROPOSED DUMPING SITE IS LOCATED AWAY FROM
RIVE/STREAM/ NALA


Junior Engineer
Const. Div. PWD Purola


Assistant Engineer
Const. Div. PWD Purola


Executive Engineer
Const. Div. PWD Purola


S.D.O. Tons.



प्रभागीय नगरपालिका
टोन्स वन प्रभाग
पुरोला (उत्तराखण्ड)


ANNEXURE-I


NAME OF WORK :-


CONSTRUCTION OF HUDOLI TO BINGADERA
MALLA MOTOR ROAD FOR STAGE-I WORK
UNDER C.D. PWD PUROLA (UTTARKASHI)


S. NO.	PARTICULARS	QUANTITY	UNIT
1	2	3	4
1	TOTAL MATERIEL RECEIVED FROM RESERVE FOREST AND CIVIL SOAM LAND DURING HILL SIDE CUTTING (QTY AS PER)		
1	RESERVE FOREST (BET X-SEC 0/0 TO 0/10)	3275.00	CUM
2	CIVIL SOAM LAND (BET X-SEC 0/11 TO 0/16)	2456.25	CUM
3	CIVIL SOAM LAND (BET X-SEC 0/22 TO 0/23)	491.25	CUM
4	CIVIL SOAM LAND (BET X-SEC 0/24 TO 0/30)	1719.37	CUM
5	CIVIL SOAM LAND (BET X-SEC 1/7 TO 1/12)	1473.75	CUM
6	CIVIL SOAM LAND (BET X-SEC 1/16 TO 1/22)	1719.37	CUM
7	CIVIL SOAM LAND (BET X-SEC 1/26 TO 1/31)	1965.00	CUM
8	RESERVE FOREST (BET X-SEC 1/32 TO 1/33)	655.00	CUM
	(CIVIL SOAM LAND RESERVE FOREST) TOTAL	13754.74	CUM
	ADD 40% SWELL FACTOR	5501.89	CUM
	G.TOTAL	19256.62	CUM
DISPOSAL LAND USE OF MATERIAL			
1	R.R STONE MASONRY LAID IN 1:5 SAND MORTAR AND LAID IN DRY	1200.50	CUM
2	R.R STONE MASONRY LAID IN DRY	800.00	CUM
3	HAND PACKED STONE FILLING	200.00	CUM
4	LAYING WIRE CRATE	2000.25	CUM
5	CONSTRUCTION OF PARAPETS	400.50	CUM
6	COLLIE WALLING	600.00	CUM
7	C.R STONE MASONRY IN 1:4 CEMENT-SAND-MORTAR	300.25	CUM
8	C.R STONE MASONRY IN 1:5 CEMENT-SAND-MORTAR	250.50	CUM
9	CONSTRUCTION OF PUCCA SCUPPER	1000.00	CUM
10	CONSOLIDATION OF SPLIT BOULDERS 6 TH THICK	2500.70	CUM
	TOTAL	9251.25	CUM
	MATERIAL DISPOSAL BY CARTAGE IN DUMPING YARD	10005.38	CUM


Junior Engineer
Const. Div. PWD Puroila


Assistant Engineer
Const. Div. PWD Puroila



Executive Engineer
Const. Div. PWD Puroila



S.D.O.
Tons Forest Division



प्रभागीय वनाधिकारी
टौन्स वन प्रभाग
पुरोला (उत्तराखण्ड)


LOCATION AND QUANTITY OF DABRIES DISPOSAL


LOCATION OF DUMPING YARD	SIZE OF DUMPING YARD	TYPE OF LAND	CAPACITY OF DUMPING YARD CUM)
0/0 TO 0/3	75X20X3	RESERVE FOREST	4500.00
0/22 TO 0/24	50X25X2.50	CIVIL SOAM LAND	3125.00
1/14 TO 1/17	75X16X2	CIVIL SOAM LAND	2400.00
		TOTAL	10025.00


Junior Engineer
Const. Div. PWD Purola


Assistant Engineer
Const. Div. PWD Purola


Executive Engineer
Const. Div. PWD Purola


S.D.O.
Tons F.D. Purola.


प्रभागीय वनाधिकारी
टौन्स वन प्रभाग
पुरोला (उत्तराखण्ड)


ANNEXURE-I


NAME OF WORK :-


CONSTRUCTION OF HUDOLI TO BINGADERA
MALLA MOTOR ROAD FOR STAGE-I WORK
UNDER C.D. PWD PUROLA (UTTARKASHI)


SUMMARY OF DABRIES DISPOSAL


S.NO.	TOTAL DABRIES	MATERIAL DISPOSAL BY CARTAGE	RE-USED MATERIAL FOR ROAD CONSTRUCTIO N	TOTAL DISPOSAL IN DUMPING ZONE	BALANCE DABRIES
1	2	3	4	5	6
1	19256.63	10005.38	9251.25	10005.38	-


 Junior Engineer
 Const. Div. PWD Purola


 Assistant Engineer
 Const. Div. PWD Purola


 Executive Engineer
 Const. Div. PWD Purola


 S. D. O.
 Tons F. D. Purola


 प्रभागीय वनाधिकारी
 टौन्स वन प्रभाग
 पुरोला (उत्तराखण्ड)


ANNEXURE-II

DETAILS OF MUCK DISPOSAL YARDS WITH LAND OWNER DETAIL

S. NO	CHAINAGE	NAME OF LAND OWNER & VILLAGE	LAND IN HEC.	LAND IN SQM.	LAND AREA BEING USED FOR DUMPING YARD	LONGITUDE	LATITUDE
1	0/0 TO 0/13	RESERVE FOREST	0.15	1500.00	1500.00	78°5'58.60"E	30°49'58.40"N
2	0/22 TO 0/24	CIVIL SOAM LAND	0.125	1250.00	1250.00	78°6'7.39"E	30°49'43.47"N
3	1/14 TO 1/17	CIVIL SOAM LAND	0.12	1200.00	1200.00	78°6'18.28"E	30°49'24.66"N



Junior Engineer
Const. Div. PWD Purola




Assistant Engineer
Const. Div. PWD Purola



Executive Engineer
Const. Div. PWD Purola




S.D.O.
Tons F.D. Purola



प्रभागीय वनाधिकारी
टोन्स वन प्रभाग
पुरोला (उत्तराखण्ड)

जोसफ अतरकाशी के अलगाल हुडीनी - खिनगेदा मल्ला मोटर रफ

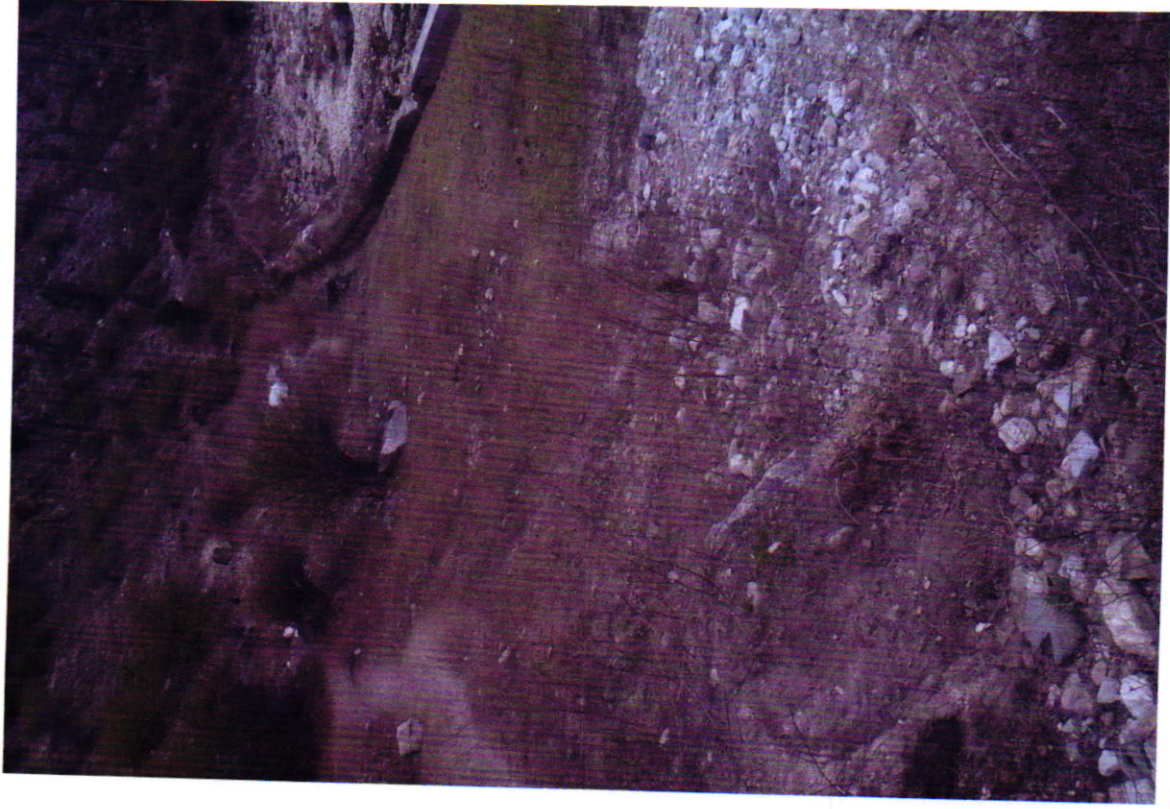

8/5/20-0/0409/3

सहायक अभियन्ता (प्रबल)
निर्माण खण्ड, लो. वि. वि.
पुरोदा

अभियन्ता अभियन्ता
निर्माण खण्ड, लो. वि. वि.
पुरोदा (उत्तराखण्ड)

अभियन्ता अभियन्ता
निर्माण खण्ड, लो. वि. वि.
पुरोदा (उत्तराखण्ड)



सू.स.ए.

४/5 नव- ०/22-200/24



०६/०५

बनागीय वनाधिकारी
टीन्स वन प्रभाग
पुरोला (उत्तराखण्ड)


सहायक अभियन्ता (ग्राम)
निर्माण खाण्ड, लो. वि. वि.
पुरोला



Handwritten signature

MSMD- 1/14 to 1/17

Handwritten signature
सहायक अभियन्ता (ग्राम)
निर्माण खण्ड, लो. वि. वि.
पुरोला

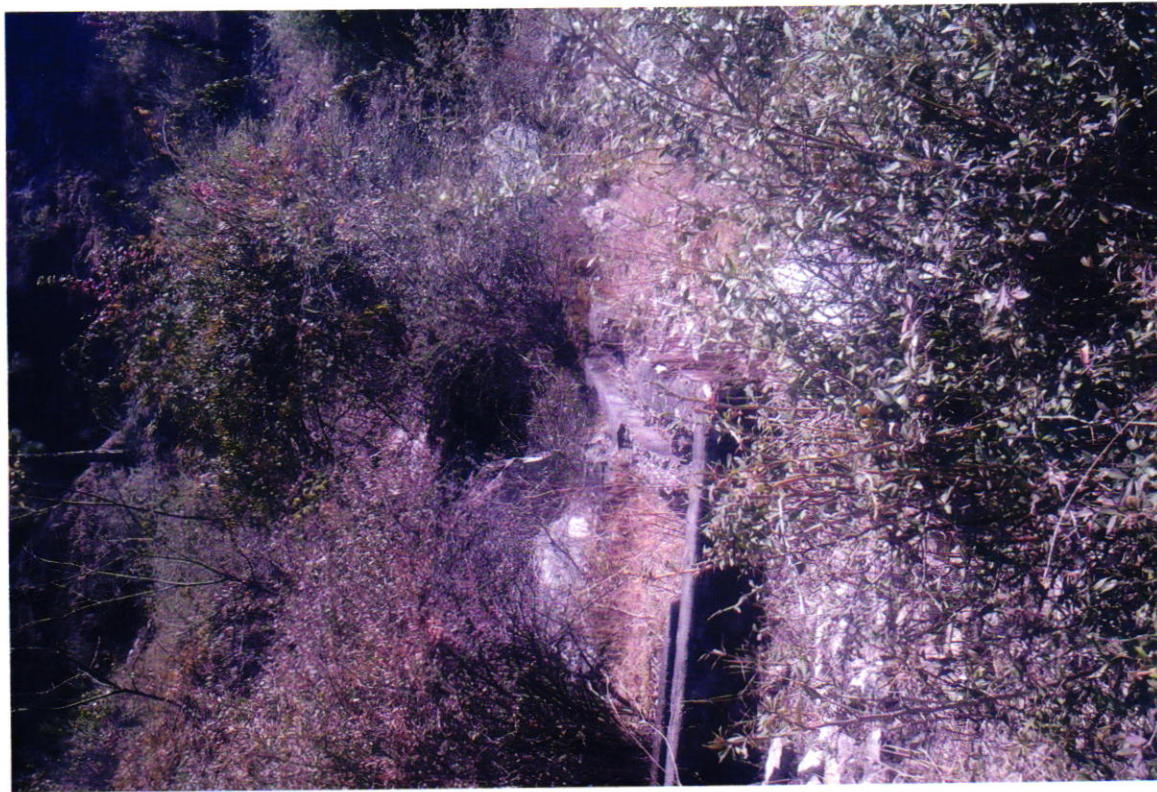

Handwritten signature

Handwritten signature
अधिक्षेत्री-समिग्रता
निर्माण खण्ड, लो. वि. वि.
पुरोला (उत्तरखण्ड)
बनगीन दण्डिकारी
दोन दण्ड प्रभाग
पुरोला (उत्तरखण्ड)
