


परियोजना का नाम : जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, डीडिहाट से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।

मलवा निस्तारण योजना



Astt. Engineer
R.E.S. P.M.G.S.Y
Didihat

परियोजना का नाम : जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, देवविछौना से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु मक डिस्पोजल प्रस्ताव।

प्रतिवेदन

प्रस्तुत प्राक्कलन देवविछौना से जमतडी मोटर मार्ग (10.525 किमी०) तक निर्माण के समय उत्सर्जित मलवे के निस्तारण हेतु गठित किया गया है। उत्सर्जित मलवे के निस्तारण हेतु स्थल चयन हेतु दिनांक 24/02/2014 को संयुक्त निरीक्षण किया गया निरीक्षण के समय मार्ग में कृषकों की नाप भूमि में चैनेज संख्या किमी 0.000, 0.460, 1.675, 2.630, 3.350, 4.200, 5.620, 6.320, 7.930, 9.730 पर स्थलों का चयन किया गया है। उक्त स्थल मार्ग के किनारे स्थित है। मलवा निस्तारण हेतु खड्ग साईड मार्ग के समानान्तर वायर क्रेट लगाये जाने का प्रावधान है तथा साईड में पत्थर की कुल वॉल बनाये जाने का प्रावधान किया गया है। कृषकों द्वारा अपनी भूमि पर मलवा निस्तारण हेतु अनापत्ति भी प्रदान की गयी है।

अतः उक्तानुसार उत्सर्जित मलवे के निस्तारण हेतु रु० 43.08 लाख का प्राक्कलन गठित किया गया है। उक्त प्राक्कलन के अनुसार ही मार्ग निर्माण के समय उक्त कार्य भी कराये जायेंगे।

अपर सहायक अभियन्ता

ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)

सहायक अभियन्ता

ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)

अधिशाली अभियन्ता

ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)

सरपंच
बन बाबायत सिरतोली
ग्राम पं० बजौर
जिला पिथौरागढ़

बन बाबायत सिरतोली
असकांड (पिथौरागढ़)

2-5

प्रपत्र 41

परियोजना का नाम : जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, डीडिहाट से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।


मक डम्पिंग प्लान/प्रमाण पत्र

प्रमाणित किया जाता है कि जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, डीडिहाट से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण से उत्पादित मलबे को उचित प्रक्रियानुसार सुरक्षित स्थान पर डम्प किया जायेगा। मलबा कहीं भी वृक्ष आच्छादित क्षेत्र जल स्रोतों में नहीं डाला जायेगा।


अपर सहायक अभियन्ता
ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)


सहायक अभियन्ता
ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)
R.E.S. Y.
Didihat


अधिसासी अभियन्ता
ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)
Rural Engineering Service
PIU-II
R.E.S. Y. Didihat


सरबन्ध
वन बंदायत सिरतौली
ग्राम पंच बाजार
जिला पिथौरागढ़


वन अधिकाारी
अम्बारा (पिथौरागढ़)

७
०१५


परियोजना का नाम : जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, देवविछौना से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु मक डिस्पोजल प्रस्ताव।

प्रमाण पत्र

मक डिस्पोजल हेतु वनीकरण एवं अभियांत्रिकी कार्यों में जो भी व्यय होगा उस ~~वनि~~ विभाग की मांग के अनुसार उपलब्ध करा दिया जायेगा।


कनिष्ठ अभियन्ता


ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)


सहायक अभियन्ता

ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)


अधिशासी अभियन्ता

ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)
Rural Engineering Service
PIU-II
PMGSY-Didihat


सरपंच

वृत्त पंचायत सिरतौली
ग्राम पंच. बाजार
जिला पिथौरागढ़



वृत्त प्रमुख (पिथौरागढ़)


आ. ६

परियोजना का नाम : जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, देवविछौना से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।

मलवे निस्तारण हेतु लाइन डायग्राम

निस्तारित बिन्दु

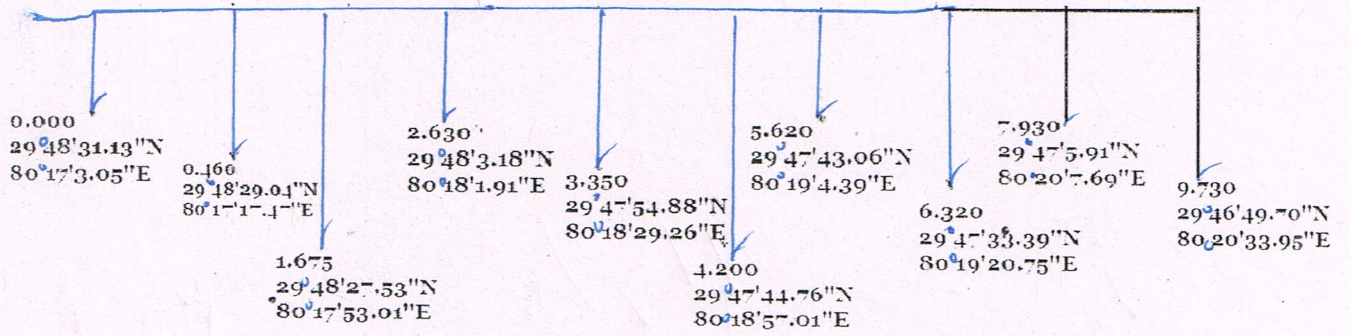

अपर सहायक अभियन्ता
ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)

सहायक अभियन्ता
ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)

अधिशाली अभियन्ता
ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)

सहसंचालक

वन संचालक सिरतोली
ग्राम पंच. बाजार
जिला पिथौरागढ़

परियोजना का नाम : जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, देवविछौना से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।

Summary of Results

- 1-The Material received from side cutting is **73558.00** Cum.
Sheet attached on page No. 88 (Muck Disposal Estimate).
- 2- The use of recived Muck in various items is **55927.76** Cum,
Sheet attached on page No. 88 (Muck Disposal Estimate).
- 3- The remaning Muck for Dumping **4407.60** Cum. Sheet attached
on page No. 88 (Muck Disposal Estimate).
- 4- Numbers of sites needed for the Dumping of Muck (Number of) 10
on page No. 90 (Muck Disposal Estimate).
- 5- Cerrying capacity of sites with Proper Dimensions is on page 89
No. (Muck Disposal Estimate).
- 6- Land ownership Report (Nap Land) on page No. 94
(Muck Disposal Estimate).
- 7- Treatment part on page No. 93 (Muck Disposal Estimate).


J.E.


A.E.
Astt. Engineer
R.E.S. P.M.G.S.Y
Didihat


E.E.
Executive Engineer
Rural Engineering Service
PIU-II
PMGSY-Didihat

प्रपत्र-41

परियोजना का नाम : जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, डीडिहाट से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।

प्रमाण-पत्र

प्रमाणित किया जाता है कि—

- 1- स्वीकृत मक डिस्पोजल प्लान के अनुसार ही मक डिस्पोजल का कार्य कराया जायेगा।
- 2- प्रस्तावित डम्पिंग साइट नदी/स्ट्रीम/नाले से दूर स्थित है।

अपर सहायक अभियन्ता

ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)

सहायक अभियन्ता

ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)

अधिशाली अभियन्ता

ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)
Rural Engineering Service
PMGSY- Didihat

सरपंच

बन पंचायत सरखोली
ग्राम (पिथौरागढ़)
जिला पिथौरागढ़

वन अधिकारी
अम्कट (पिथौरागढ़)

21/5/19

Rate Card

Block 52 Didihat (PITHORAGARH)

Effective Date 16/05/2014

Item Description		Rate In (Rs.)	
		Rate	Unit
	Construction of retaining walls/breast walls in cement mortar 1:5 as per drawing and technical specifications Clause 1604		
77636 8-4-1	Earthwork in excavation for structures	244.50	cu.m
77637 8-4-2	Plain cement concrete M 10 grade	5,777.50	cu.m
77638 8-4-3	Stone masonry in cement mortar 1:5	3,130.10	cu.m
77639 8-4-4	Pointing with cement mortar 1:3	66.30	sq.m
77640 8-4-5	Providing P.C.C. M 20 architectural coping on top of retaining wall/breast wall	452.20	metre
77641 8-4-6	Filter material behind retaining wall / breast wall as per Specification 1204.3.8 in a width of 600 m	3,803.70	cu.m
77642 8-4-7	Back filling behind retaining wall/breast wall	599.50	cu.m
8-5	Construction of Hill Side Drain		
	Construction of hill side drain in accordance with the requirement of specifications true to lines and grades. Dimesions and other particulars as per drawing and Technical Specification Clause 1606.1		
77643 8-5-1	Earthwork in excavation for structures as per drawing and technical specification	244.50	cu.m
77644 8-5-2	Plain cement concrete M10 grade	5,783.50	cu.m
77645 8-5-3	Stone masonry in cement mortar 1:5	3,130.10	cu.m
77646 8-5-4	Plain cement concrete M15 grade	5,707.60	cu.m
77647 8-5-5	Cement plaster 15 mm thick 1:4 on stone masonry	174.80	sq.m
77648 8-5-6	Providing P.C.C. M20 architectural coping on top of wall	452.20	metre
8-6	Construction of Catch Water / Intercepting Drain		
	Construction of catch water/intercepting drain in random rubble masonry in 1:5 cement mortar true to the specified lines grades levels and dimensions as per the requirement of the specifications Clause 1606.2		
77649 8-6-1	Earthwork in excavation for structures as per drawing and technical specification	244.50	cu.m
77650 8-6-2	Plain cement concrete M10 grade	5,783.50	cu.m
77651 8-6-3	Stone masonry in cement mortar 1:5	3,130.10	cu.m
77652 8-6-4	Plain cement concrete M15 grade	5,707.60	cu.m
77653 8-6-5	Cement plaster 15 mm thick 1:4 on stone masonry	174.80	sq.m
77654 8-6-6	Providing P.C.C. M 20 architectural coping on top of wall	452.20	metre
8-7	Construction of Scupper		

A.E.R.E.S.
P.I.U.-P.M.G.S.Y.
Didihat

Executive Engineer
Rural Engineering Service
P.M.G.S.Y.- Didihat

Rate Card		Block 52 Didihat (PITHORAGARH)	Effective Date 16/05/2014	
Chapter Name	Other Item			
Item Description			Rate In (Rs.)	
			Rate	Unit
75476 16-1	Excavation in foundation for retaining & breast walls in all types of soils and rocks including lead, lift and disposal of surplus material as per direction of engineer - in - charge		244.80	cu.m
75477 16-2	Random rubble stone masonry laid in mud mortar .(As per PWD Uttarakhand specifications)		1,754.40	cu.m
75478 16-3	Random Rubble Masonary laid dry in breast wall,retaining wall, parapets,scupper etc. Including supply of all materials,labour,t & p& royalty etc,required for proper complition of work.(As per PWD Uttarakhand specifications)		1,563.00	cu.m
75479 16-4	H.P stone filling in back of wallls including cost of all materials ,royalty.t&p etc. complete.		600.20	cu.m
75480 16-5	Random Rubble Stone Masonry laid in 1:6 cement and sand mortar, in breast walls, retaining walls, parapets, scuppers, etc. including supply of all material, labour, T&P and royalties etc.(As per PWD Uttarakhand specifications)		2,838.20	cu.m
75481 16-6	Random Rubble stone masonary in Coolie walling including supply of all material, labour, T&P etc. required for proper completion of the work.(As per PWD Uttarakhand specifications)		1,183.00	cu.m
75482 16-7	Cement plum masonry with 40% plum & 60% 1:3:7 cement concrete including supply of all material, labour, T&P etc. required for proper completion of the work. (As per PWD Uttarakhand specifications)		4,726.10	cu.m
75483 16-8	Supply and fabrication of steel truss bridge as per detailed drawing attached including supply of all structural steel confirming IS 226 - 1969 required for proper completion of the bridge including ground erection of the bridge and one coat of approved quality anticorrosive (red oxide) paint of confirming IS 5660, all T&P, nuts and bolts, washers and also including supply and fixing of shop rivets required as per drawing, required equipment shall be arranged by the contractor at his own cost which shall be taken back by the contractor after satisfactory execution of the job, the rates shall include ground erection in the workshop and its dismentling after inspection, approval and removing defects, match marking of all parts, numbering and proper stacking in the premises of workshop before cartage to site of work. The work shall be executed in accordance to IS - 1915. The rates shall include cost of all material, its wastage, cutting, bending if required, welding, making holes, shop riveting, labour, T&P etc. required for proper completion of the work.		81,849.00	M.T.
16-9	Wire Crates As per PWD Uttarakhand Specifications			
16-9-1	Wirecrates In Nos.			
75484 16-9-1-1	Providing and laying of wire crates 3.00x1.50x1.50 in size with a 10 gauge BWG GI wire conforming to IS: 280 & IS:4826 in 150mm x 150mm mesh laid with stone boulders weighing not less than 25 kg each.(As per PWD Uttarakhand Specification)		8,944.80	Nos.
75485 16-9-1-2	Providing and laying of wire crates 3.00x1.50x1.50 in size with a 8 gauge BWG GI wire conforming to IS: 280 & IS:4826 in 150mm x 150mm mesh laid with stone boulders weighing not less than 25 kg each.(As per PWD Uttarakhand Specification)		10,350.90	Nos.
Roads & Bridges Uttarakhand - 2014-2015 - 16/05/2014				
Page 64 of 99				
17/05/14 10:34				

A.E.R.E.S.
P.I.U.- P.M.G.S.Y.
Didihat

Executive Engineer
Rural Engineering Service
P.M.G.S.Y.- Didihat

A.A.E.

Rate Card Block 52 Didihat (PITHORAGARH)

Effective Date 16/05/2014

Chapter Name PROTECTION WORKS

Item Description		Rate In (Rs.)	
		Rate	Unit
77862 14-1	Providing and laying boulder apron for bed protection with stone boulders of minimum size and weight as per Table 1300.1, no fragment weighing less than 25 kg laid dry complete as per drawing and technical specifications Clause 1301	1,212.90	cu.m
77863 14-2	Providing and laying of boulder apron laid in wire crates with 4 mm dia GI wire conforming to IS:280 and IS:4826 in 100 mm x 100 mm mesh (woven diagonally) including 10 per cent extra for laps and joints laid with stone boulders weighing not less than 25 kg each as per drawing and technical specifications Clause 1301	2,021.40	cu.m
77864 14-3	Providing and laying of apron with cement concrete blocks of size as per Table 1300.1 cast-in-situ and made with nominal mix of M-15 grade cement concrete as per drawing and technical specifications Clause 1301	5,803.20	cu.m
14-4	Single bamboo palasiding / walling of whole 2nd class bamboo (Jati or Bethua) 75mm dia and closely packed & driven including fitting fixing with half bamboo kamis horizontally in three rows with cane or tying with wire complete and struts 1.5 m apart longitudinally and providing brush wood as per drawing and technical specifications Clause 1302.5		
77865 14-4-A	Driven at least 900 mm below ground and 1200 mm above ground	621.60	metre
77866 14-4-B	Driven at least 900 mm below ground and 900 mm above ground on average	481.70	metre
14-5	Providing and laying pitching on slopes laid over prepared filter media as per drawing and technical specifications Clause 1302		
77867 14-5-1	Stone/Boulder	1,212.90	cu.m
77868 14-5-2	Cement concrete blocks of size as per Table 1300.2 cast in cement concrete of grade M 15	5,803.20	cu.m
77869 14-5-3	Brick pitching set in cement mortar 1:4	7,648.60	cu.m
77870 14-6	Providing and laying filter material underneath pitching in slopes complete as per drawing and technical specifications Clause 1302	1,989.60	cu.m
14-7	Providing and laying flooring laid over cement concrete bedding complete as per drawing and technical specification Clause 1303		
77871 14-7-1	Rubble stone laid in cement mortar 1:3	3,893.20	cu.m
77872 14-7-2	Cement concrete blocks grade M 15	5,746.30	cu.m
77873 14-7-3	Brick on edge laid in cement mortar (1:3)	7,384.70	cu.m
77874 14-8	Providing and laying of dry rubble flooring complete as per drawings and technical specifications Clause 1303.3	1,929.30	cu.m
77875 14-9	Providing and laying curtain walls complete as per drawing and technical specification Clause 1304	17,852.60	cu.m
77876 14-10	Construction of flexible apron 1 m thick comprising of loose stone boulders	1,246.30	cu.m

MORD - 2014-2015 - 16/05/2014 - 14

Page 53 of 58

28/05/14 9:57


 A.A.E.


 A.E.R.E.S.
 P.I.U.- P.M.G.S.Y.
 Didihat


 Executive Engineer
 Rural Engineering Service
 P.M.G.S.Y.- Didihat

1-परियोजना का नाम:- जनपद मिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित,देवविहरीना से जमताडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।

Name of Block:-Didihat

Length:10.525KM

Muck Received From Hill Side Cutting

Sr.No.	Description of work	Quantity	Unit
	Material recived from hill side cutting (1*1/2*10.525*1000*6.00*2.33)	73558.00	Cum

Disposal and use of Material

1	Earth and Boulder filling for re-grading	7355.80	cum
2	Earth and Boulder filling for Super elevation	0.00	cum
3	Construction of coolie walling	2250.00	cum
4	R.R. Stone Mesonary laid in 1:5	2874.50	cum
5	R.R. Stone Mesonary laid in Dry	8595.67	cum
6	Hand Packed Stone Filling	5268.26	cum
7	Construction of Wire Create(883.13+792.00)	1675.13	cum
8	Making of Edge Stone	0.00	cum
9	Construction of Parapet	109.61	cum
11	Construction of Pillars	20.40	cum
12	Construction of Scupper	3100.68	cum
13	Material Used for hill side pucca k/c drain (Quantity=2150mt)(@0.167cum/mt)	83.33	cum
14	Providing and laying using gravel in soft reaches(G.S.B.)	5117.36	cum
15	Qty of Material to be disposed along the Road (10.000*750*2.50*1.0)	18750.00	cum
16	P/L M 25	178.46	
17	P/L M 10	123.03	
18	C.R. Stone masonary laid in 1:4 cement:sand mortar for abutment.	425.49	cum
TOTAL		55927.76	cum


Quantity of Muck to be disposed at dumping places = (Material Received- Material used) cum


73558.00 - 55927.76 = 17630.24

Add for Bulkege 25% extra = 4407.6 cum

22037.7955




AERES
P.I.U.-P.M.G.S.Y
Didihat


Executive Engineer
Rural Engineering Service
P.M.G.S.Y.- Didihat


अवधि अधिकारी
अस्साव (विश्वी गणक)


अवधि अधिकारी

Estimate for Muck Disposal

1-परियोजना का नाम:- जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, देवविछौना से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।

Name of Block: Munsiyari (Pithoragarh)

Length: 6.000 KM

Detail Of Measurement

Sr.No.	Item Of Work	No.	Length	Width	Height	Quantity	Unit
1).	Earthwork in excavation for structures, Construction of retaining walls/breast walls in cement mortar 1:5 as per drawing and technical specifications Clause 1604						
1	0.000	1 x 9	3.00	1.50	0.50	20.25	cum
2	0.460	1 x 10	3.00	1.50	0.50	22.50	cum
3	1.675	1 x 9	3.00	1.50	0.50	20.25	cum
4	2.630	1 x 6	3.00	1.50	0.50	13.50	cum
5	3.350	1 x 8	3.00	1.50	0.50	18.00	cum
6	4.200	1 x 8	3.00	1.50	0.50	18.00	cum
7	5.620	1 x 8	3.00	1.50	0.50	18.00	cum
8	6.320	1 x 8	3.00	1.50	0.50	18.00	cum
9	7.930	1 x 9	3.00	1.50	0.50	20.25	cum
10	9.730	1 x 7	3.00	1.50	0.50	15.75	cum
TOTAL						184.50	cum
2).	Providing and laying of boulder apron laid in wire crates with 4 mm dia GI wire conforming to IS:280 and IS:4826 in 100 mm x 100 mm mesh (woven diagonally) including 10 per cent extra for laps and joints laid with stone boulders weighing not less than 25 kg each as per drawing and technical specifications Clause 1301						
1	0.000	1 x 6	3.00	1.50	1.50	40.500	cum
	2nd	1 x 6	3.00	1.25	1.50	33.750	cum
2	0.460	1 x 7	3.00	1.50	1.50	47.250	cum
	2nd	1 x 7	3.00	1.25	1.50	39.375	cum
3	1.675	1 x 6	3.00	1.50	1.50	40.50	cum
	2nd	1 x 6	3.00	1.25	1.50	33.75	cum
4	2.630	1 x 7	3.00	1.50	1.50	47.25	cum
	2nd	1 x 7	3.00	1.25	1.50	39.38	cum
5	3.350	1 x 6	3.00	1.50	1.50	40.50	cum
	2nd	1 x 6	3.00	1.25	1.50	33.75	cum
6	4.200	1 x 8	3.00	1.50	1.50	54.00	cum
	2nd	1 x 8	3.00	1.25	1.50	45.00	cum
7	5.620	1 x 7	3.00	1.50	1.50	47.25	cum
	2nd	1 x 7	3.00	1.25	1.50	39.38	cum

J.E.

जन श्रमिकारी
आयुक्त (पिथौरागढ़)

A.E.

Astt. Engineer
R.E.S. P.M.G.S.Y
Didihat

Executive Engineer
Rural Engineering Serv.
PIU-II
P.M.G.S.Y-Didihat

8	6.320	1	x	6	3.00	1.50	1.50	40.50	cum
	2nd	1	x	6	3.00	1.25	1.50	33.75	cum
9	7.930	1	x	5	3.00	1.50	1.50	33.75	cum
	2nd	1	x	5	3.00	1.25	1.50	28.13	cum
10	9.730	1	x	6	3.00	1.50	1.50	40.50	cum
	2nd	1	x	6	3.00	1.25	1.50	33.75	cum
TOTAL								792.00	cum
3).	Random Rubble stone masonry in Coolie walling including supply of all material , labour, T&P etc. required for proper completion of the work. (As per PWD Uttarakhand specifications)	10	x	10	75.00	0.50	0.60	2250.00	cum
								2250.00	cum

मन अकाधिकारी
अभियन्ता (विश्वीय)

अ-ए

अ.ए.
Asst. Engineer
R.E.S. P.M.G.S.Y
Didihat

अ.ए.
Executive Engineer
Rural Engineering Service
R.E.S. P.M.G.S.Y
Didihat

Estimate for Muck Disposal					
1-परियोजना का नाम:- जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, देवविछौना से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।					
Name of Block: Didihat			Length:-10.525 KM		
Bill Of Quantity					
Sr.No.	Item Of Work	Quantity	Unit	Rate	Amount
1).	Earthwork in excavation for structures, Construction of retaining walls/breast walls in cement mortar 1:5 as per drawing and technical specifications Clause 1604	184.50	Cum	244.50	45110.25
2).	Providing and laying of boulder apron laid in wire crates with 4 mm dia GI wire conforming to IS:280 and IS:4826 in 100 mm x 100 mm mesh (woven diagonally) including 10 per cent extra for laps and joints laid with stone boulders weighing not less than 25 kg each as per drawing and technical specifications Clause 1301	792.00	Cum	2021.40	1600948.80
3).	Random Rubble stone masonry in Coolie walling including supply of all material, labour, T&P etc. required for proper completion of the work. (As per PWD Uttarakhand specifications)	2250.00	Cum	1183.00	2661750.00
Total					4307809.05
Say					43.08

चार सौ वरुण प्रजापति कारखाना व संरक्षण

270 टन डस्ट चार्ज

3.50

46.58

10.93

47.51

A.A.E.

जन शोभाधिकारी
प्रशासन (विशेष)

अ.र.

Astt. Engineer Executive Engineer
R.E.S. P.M.S. Rural Engineering S
Didihat
PIO-II
P.M.S.Y. Didihat

अ

1-परियोजना का नाम:- जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, देवविछौना से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।

Name of Block- Didihat

Length: 10.525KM

Details of Vegetation Plantation Area in Muck Disposal point

Chainage of area	Length	width	Area	Unit
0.000	18.00	18.00	324.00	sqm
0.460	21.00	15.00	315.00	sqm
1.675	18.00	15.00	270.00	sqm
2.630	21.00	20.00	420.00	sqm
3.350	18.00	25.00	450.00	sqm
4.200	24.00	20.00	480.00	sqm
5.620	24.00	20.00	480.00	sqm
6.320	21.00	20.00	420.00	sqm
7.930	21.00	20.00	420.00	sqm
9.730	18.00	18.00	324.00	sqm
Area			3903.00	sqm
Total Area = (Area/10000)			0.390	hect.

Total area = 0.390 Hect.

J.E

A.E
Asst. Engineer
R.E.S. P.M.G.S.Y
Didihat

E.E
Executive Engineer
Rural Engineering Service
PMGSY-Didihat

अन्य अधिकारी
अतिरिक्त (विशेष कार्य)

दि. 15.11.2017

Name of Project :- Contruction of Didihat (Devichona) to Jamtari M/R (Km 10.525)

मलवा निस्तारण हेतू सिविल सोयम भूमि

क्र० सं०	खाता न०	खसरा न०	कुल रकवा	अर्जित रकवा	भूमि का प्रकार	मौजा	विवरण
1	76	10112	0.155	0.032	ब०का० आ०	खेतार कन्ययाल	सिविल सोयम
2	76	10703	0.376	0.032	ब०का० आ०	खेतार कन्ययाल	सिविल सोयम
3	76	10704	0.501	0.027	ब०का० आ०	खेतार कन्ययाल	सिविल सोयम
4	76	10721	0.561	0.042	ब०का० आ०	खेतार कन्ययाल	सिविल सोयम
5	76	11304	0.381	0.045	ब०का० आ०	खेतार कन्ययाल	सिविल सोयम
6	18	1614	2.017	0.048	ब०का० आ०	सिरतोली	सिविल सोयम
7	76	2770	0.875	0.048	ब०का० आ०	सिरतोली	सिविल सोयम
8	4	1507	3.295	0.042	ब०का० आ०	जमतडी	सिविल सोयम
9	18	1540	0.630	0.042	ब०का० आ०	जमतडी	सिविल सोयम
10	4	1515	0.280	0.032	ब०का० आ०	जमतडी	सिविल सोयम
योग				0.390	है०		


Junior Engineer
Irrigation Div. P.W.D.
Pithoragarh


Assistant Engineer
Irrigation Div. P.W.D.
Pithoragarh


Executive Engineer
Irrigation Div. P.W.D.
Pithoragarh

Estimate for Muck Disposal

1-परियोजना का नाम:- जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, देवविछौना से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।

Name of Block:Munsiyari(Pithoragarh)			Length:10.525 KM			Type of land U.K. Govt. CIVIL SOYAN
Chainage	Area(sqm)	Length	Width	Coordinate		
				Latitude(N)	Logitude(E)	
0.000	756.00	27.00	28.00	29°48'31.13"N	80°17'3.05"E	— do —
0.460	780.00	30.00	26.00	29° 48'29.04"N	80°17'17.47E	— do —
1.675	675.00	27.00	25.00	29° 48'27.53"N	80°17'53.01"E	— do —
2.630	360.00	18.00	20.00	29°48'3.18"N	80°18'1.91"E	— do —
3.350	600.00	24.00	25.00	29°47'54.88"N	80°18'29.26"E	— do —
4.200	528.00	24.00	22.00	29°47'44.76"N	80°18'57.01"E	— do —
5.620	600.00	24.00	25.00	29°47'43.06"N	80°19'4.39"E	— do —
6.320	528.00	24.00	22.00	29°47'33.39"N	80°19'20.75"E	— do —
7.930	675.00	27.00	25.00	29°47'5.91"N	80°20'7.69"E	— do —
9.730	420.00	21.00	20.00	29°46'49.70"N	80°20'33.95"E	— do —

JE

AE
Asth. Eng.
R.E.S. P.M.G.S.Y
Didihat

EE
Executive Engineer
Rural Engineering Service
PIU-II
P M G S Y-Didihat

जन श्रमिकता
कार्य (पिथौरागढ़)

७
२६

प्रपत्र-41

परियोजना का नाम : जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, डीडीहाट से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।

फोटो ग्राफ

Name of work : Construction of Devichhona to Jamtadi (Stage I) motor road under PMGSY

Name of Block : Kanalichina (Pithoragarh)

Length : 10.525 Km



Km - 0.000



Km - 0.460

सर्वेक्षक
प्रमुख (पिथौरागढ़)
२५



Km - 1.675

सर्वेक्षक
वन पंचायत सिरतोली
ग्राम सं. बाजार
जिला पिथौरागढ़

५
A-A-E-

Astt. Engineer
R.E.S. PMGSY

Executive Engineer
Rural Engineering Service
P.M.G.S.Y.- Didihat

Name of work : Construction of Devichhona to Jamtadi (Stage I) motor road under PMGSY

Name of Block : Kanalichina (Pithoragarh)

Length : 10.525 Km



Km - 2.630



Km - 3.350

जन प्रशिक्षिका
असकाव (पिथौरागढ़)
४-५



Km - 4.200

सरपंच
वन पंचायत सिरतोली
पंचायत बाजार
जिला पिथौरागढ़

AAE

Asst. Engineer
R.E.S. PMGSY
D.D.

Executive Engineer
Rural Engineering Service
P.M.G.S.Y. - Didihat

Name of work : Construction of Devichhona to Jamtadi (Stage I) motor road under PMGSY

Name of Block : Kanalichina (Pithoragarh)

Length : 10.525 Km



Km - 5.620



Km - 6.320

अ.प्र.प्र.प्र.प्र.प्र.
अ.प्र.प्र.प्र.प्र.प्र.
अ.प्र.प्र.प्र.प्र.प्र.



Km - 7.930

अ.प्र.प्र.प्र.प्र.प्र.
अ.प्र.प्र.प्र.प्र.प्र.
अ.प्र.प्र.प्र.प्र.प्र.

Executive Engineer
Rural Engineering Service
P.M.G.S.Y.- Didihat

Asst. Engineer
R.E.S. PMGSY
Didihat

A.A.E.

Name of work : Construction of Devichhona to Jamtadi (Stage I) motor road under PMGSY

Name of Block : Kanalichina (Pithoragarh)

Length : 10.525 Km

Km - 9.730



घन अंशिकाती
आम्हाट (पिथौरागढ)

अ. ध.

सरपंच


वन पंचायत सिरतोली
ग्राम पं. वाजाण
जिला पिथौरागढ

Executive Engineer
Rural Engineering Service
PIO-II
PMGSY-Didihat

अ. ध.
R.E.S. PMGSY
Didihat

A.A.E

परियोजना का नाम : जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, डीडिहाट से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।

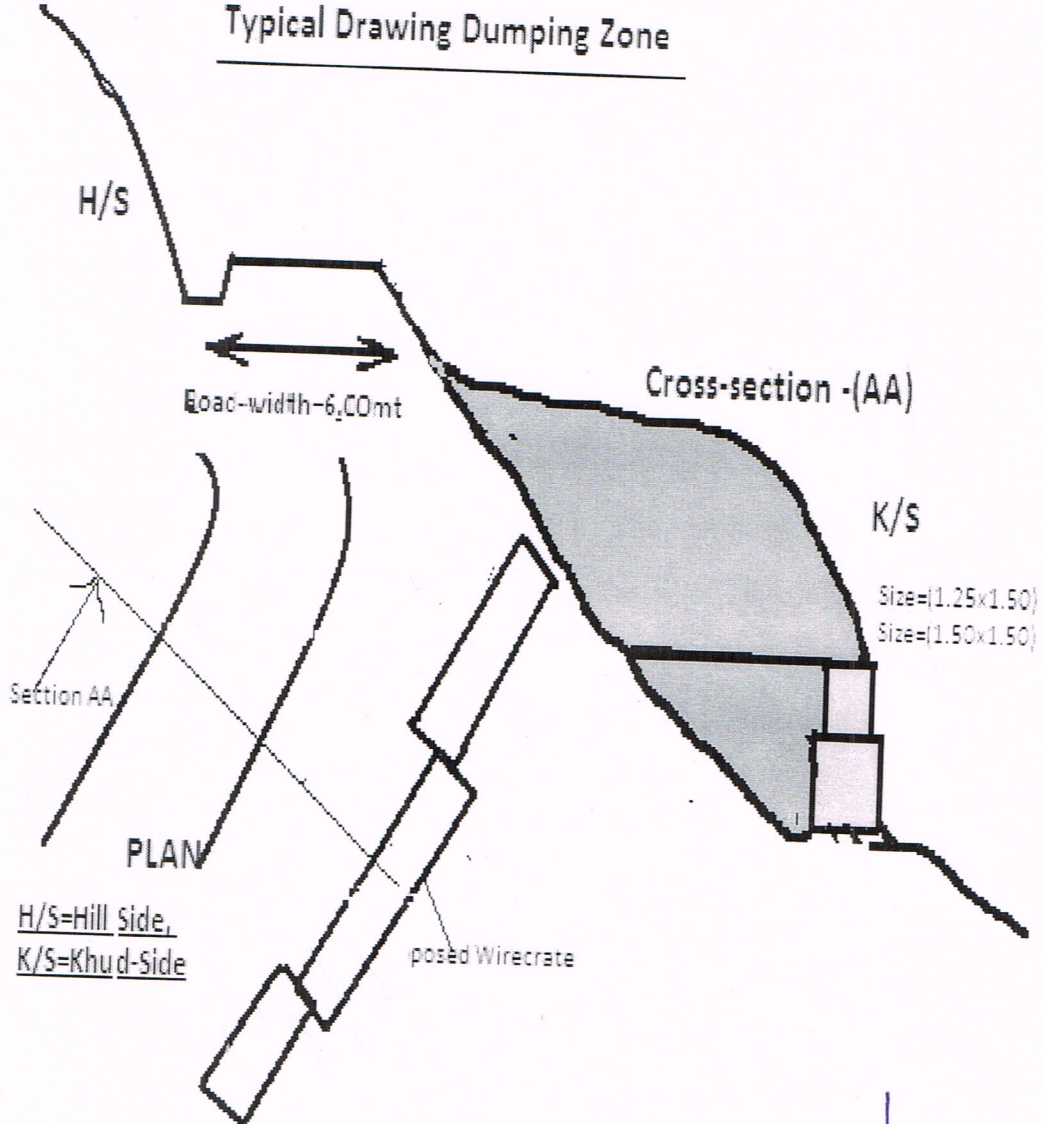

अधिकारी
अस्कोट (पिथौरागढ़)

अ.स.स.

कनिष्ठ अभियन्ता

ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)

सहायक अभियन्ता



ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)
R.E.S. P.M.G.S.Y
Didihat

अधिशाली अभियन्ता

ग्रामीण अभियन्त्रण सेवा विभाग,
पी०आई०यू०, पी०एम०जी०एस०वाई०
डीडीहाट (पिथौरागढ़)
Rural Engg. Service
PMGSY-II
PMGSY-Didihat

परियोजना का नाम : जनपद पिथौरागढ़ में प्रधानमंत्री ग्राम सड़क योजना के अन्तर्गत प्रस्तावित, डीडिहाट से जमतडी मोटर मार्ग (10.525 कि०मी०) तक का नव निर्माण हेतु वन भूमि हस्तान्तरण प्रस्ताव।

Typical Drawing Dumping-Zone

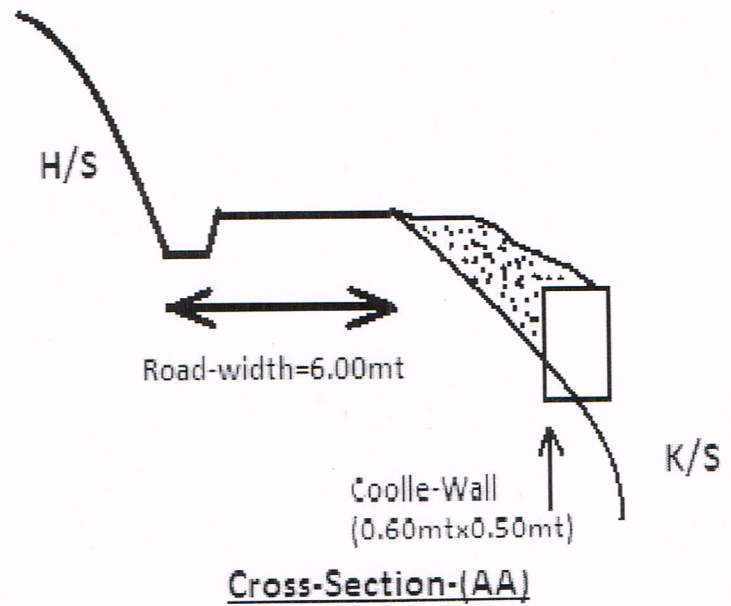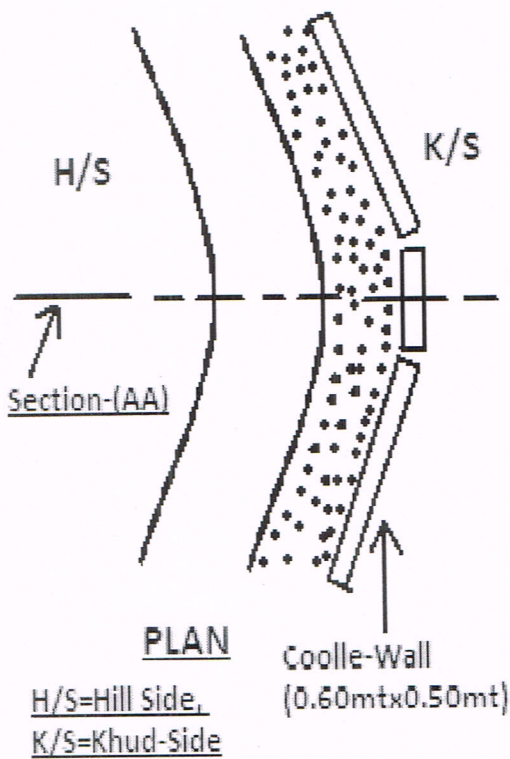

A.A.E.

Astt. Engineer
 R.E.S. P.M.G.S.Y
 Didihat

असहायक अभियंता
 अस्सी (पिथौरागढ़)

अ.स.

Executive Engineer
 Rural Engineering Service
 PIU-II
 RMGSY-Didihat
