

परियोजना का नाम :- जनपद रुद्रप्रयाग के विकासखण्ड अगस्त्यमुनि में जिला योजना के अन्तर्गत चोपडा उडामाण्डा (पीएमजीएसवाई) मोटर मार्ग से बनवालधार (जरम्वाड) होते हुए बैजी काण्डई (अनु० बस्ती) तक मोटर मार्ग के निर्माण हेतु लोक निर्माण विभाग को वनभूमि हस्तान्तरण प्रस्ताव, लम्बाई 2.05 किमी०


मक डिस्पोजल प्लानिंग

A (i)	Material recived from hill side cutting (Civil Van Panchayat land) $(1/2 \times 2050 \times 5.95 \times 3.00) =$	9817.50	cum
A (ii)	Material recived from hill side cutting (Naap land) $(1/2 \times 900 \times 5.95 \times 2.00) =$	5355.00	cum
	Total A	15172.50	Cum
B	Material received from hill side cutting including 40% of swell factor	6069.00	cum
A+B	Material to be Disposedl by Cartage	21241.50	Cum
	Material Re-used in the project after 40% swell factor of A+B		
1	R.R. Stone Masonary laid in 1:6	1300.00	cum
2	R.R. Stone Masonary laid dry	1800.00	cum
3	Hand packed Stone filling	800.00	cum
4	Construction of Wire crate	3000.00	cum
5	Construction of Parapet	458.65	cum
6	Granular sub base /base/surface	250.00	cum
7	Construction of Scupper	1500.00	cum
8	Construction of Road side Drain	100.00	cum
9	Super elevation & Patri filling	150.00	cum
10	Concrete work	200.00	cum
11	Total	9558.65	cum

Summary of Dabries Disposal

Sr. No.	Total Dabries	Material disposal by Cartage	Reused material for road construction	Total disposal in Dumping Zone
1	21241.50 Cum	11682.82 Cum	9558.65 Cum	11682.82 Cum (55.00%)


Junior Engineer
Prov. Div. PWD
Rudraprayag



Assistant Engineer
Prov. Div. PWD
Rudraprayag


Executive Engineer
Prov. Div. PWD
Rudraprayag

परियोजना का नाम :- जनपद रुद्रप्रयाग के विकासखण्ड अगस्त्यमुनि में जिला योजना के अन्तर्गत चोपडा उडामाण्डा (पीएमजीएसवाई) मोटर मार्ग से बनवालधार (जरम्वाड) होते हुए बैजी काण्डई (अनु० बस्ती) तक मोटर मार्ग के निर्माण हेतु लोक निर्माण विभाग को वनभूमि हस्तान्तरण प्रस्ताव, लम्बाई 2.05 किमी०

Detail of Muck Disposal Sites

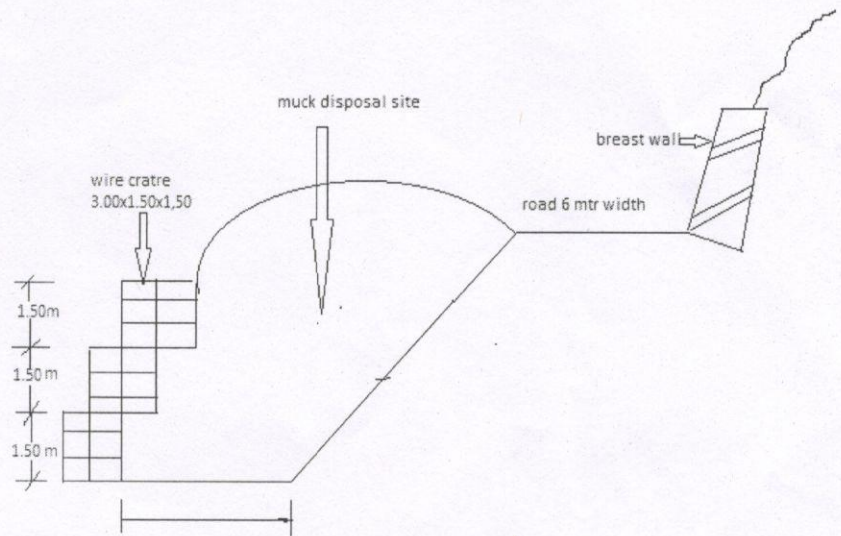
S. No.	Location of Dumping Yard)	Owner of Land	Area (in hectares)	Height of Dumping Zone (m)	Capacity of Dumping yard in cum	longitude /latitude
1	0/0	Naap Land	0.0125	8.00	1000.00	79° 7' 17.02" E 30° 20' 26.81" N
2	0/25	Naap Land	0.0125	8.00	1000.00	79° 7' 16.17" E 30° 20' 31.9" N
3	1/3	Naap Land	0.0325	15.00	4875.00	79° 6' 59.16" E 30° 20' 22.33" N
4	1/35	Naap Land	0.0325	15.00	4875.00	79° 6' 55.88" E 30° 20' 4.41" N
	Total		0.0900		11750.00	


Junior Engineer
Prov. Div. PWD
Rudraprayag


Assistant Engineer
Prov. Div. PWD
Rudraprayag


Executive Engineer
Prov. Div. PWD
Rudraprayag

Muck Disposal cross section



[Signature]
S.E.

[Signature]
AE

E.E
P.D.P.W.D
RUDRAPRAYAG
